



Hunters Point Naval Shipyard Environmental Cleanup (Building Demolition) Program Update

**Hunters Point Shipyard Citizens Advisory Committee
Business and Employment Subcommittee Meeting**

April 16, 2026

Michael Pound – BRAC Environmental Coordinator
&
ECC Infrastructure LLC

Agenda

| Topic |
|---------------------------------------------------------------------------------------|
| • Introductions |
| • Parcel G Building Demolition Task Order Award (ECC) |
| • Task Order Organizational Responsibilities |
| • Schedule Update |
| • Building Demolition Progress |
| • Navy Parcel G Contract 23% Local Hiring and Subcontracting Requirements |
| • Internships |
| • Next CAC Meeting |
| • Future Opportunities |
| • Government Oversight of Meeting Local Hiring and Subcontracting Requirements (Navy) |
| • New HPNS Building Demolition Multiple Award Construction Contract (Navy) |
| • Contacts |
| • Questions |



Parcel G Building Demolition ECC

Task Order – Organizational Responsibilities

- NAVFAC BRAC – Defined the Parcel G contract project requirements, including the 23% for local business subcontracting and D-10 resident hiring requirements
- NAVFAC Southwest – Awarded the task order on April 23, 2025
- NAVFAC Southwest/Resident Officer in Charge of Construction (ROICC) Office - Responsible for TO management and compliance monitoring of meeting the 23% requirements
- ECC – Responsible for meeting the 23% requirements and implementation

Parcel G TO: Field Work Schedule

| | Feb 2026 | Mar 2026 | Apr 2026 | May 2026 | Jun 2026 | Jul 2026 | Aug 2026 | Sep 2026 | Oct 2026 | Nov 2026 | Dec 2026 | Jan 2027 | Feb 2027 | Mar 2027 | Apr 2027 | May 2027 | Jun 2027 | Jul 2027 |
|---------------|----------|----------|----------|----------|----------|----------|----------|----------|----------|----------|----------|----------|----------|----------|----------|----------|----------|----------|
| Building 351 | ✓ | ✓ | | | | | | | | | | | | | | | | |
| Building 351A | ✓ | ✓ | | | | | | | | | | | | | | | | |
| Building 366 | | ✓ | | | | | | | | | | | | | | | | |
| Building 401 | | | | | | | | | | | | | | | | | | |
| Building 411 | | | | | | | | | | | | | | | | | | |
| Building 439 | | | | | | | | | | | | | | | | | | |
| Pad 408 | | | | | | | | | | | | | | | | | | |

Hazardous Materials Abatement

Demolition



Parcel G Demolition Approach (No Explosives)

- 1 Hazardous Materials Removed First
 - Abatement completed prior to demolition
- 2 Mechanical Demolition Only
 - Excavators, shears, heavy equipment
 - NO explosives used ★
 - Per RFP Part 6, Attachment D, Sheet OS001, Note 16
- 3 Controlled, Phased Removal
 - Buildings removed systematically
 - Dust and air monitoring ongoing




Six buildings will be removed
at Parcel G

Parcel G Building Air Monitoring Program

Air monitoring program has begun with real-time dust reading and analytical sampling during all abatement and demolition activities

Air Monitoring Station #1

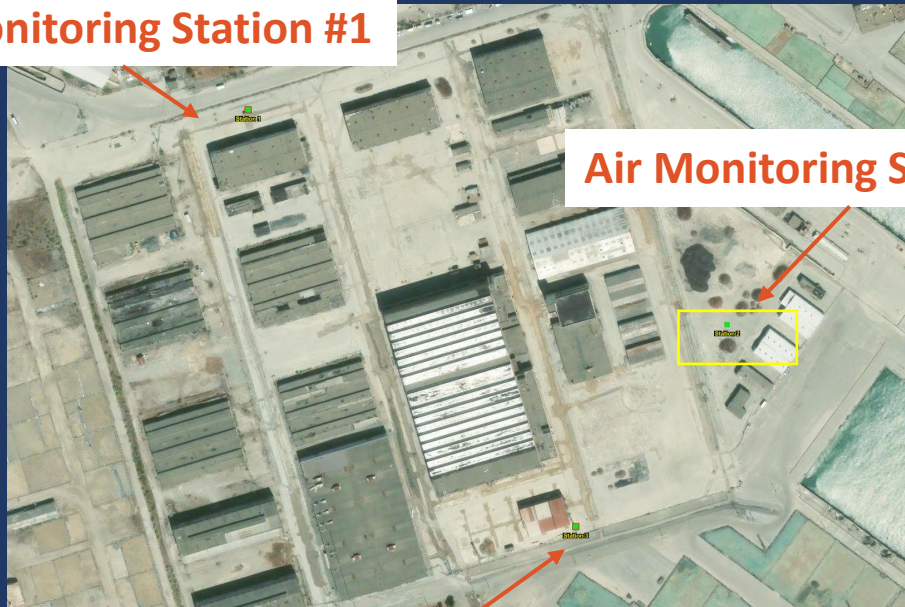

Air Monitoring Station #2



Air Monitoring Station #1

Air Monitoring Station #3

What We Monitor – When and Why


✓ Monitored During All Work Activities

- ✓ Asbestos
- ✓ Lead
- ✓ Manganese
- ✓ Total Suspended Particulates (TSP)
- ✓ Particulate Matter 10 μ g (PM-10)



Additional Monitoring During Demolition


- ✓ Cesium-137
- ✓ Plutonium-239/240
- ✓ Radium-226
- ✓ Strontium-90
- ✓ Thorium-232
- ✓ Uranium-235
- ✓ Mercury*
- ✓ Polychlorinated Biphenyls (PCBs)*



* = Open Air Demolition (Buildings 401 & 411)

Parcel G Building Demolition Progress

Hazardous materials abatement has begun with Asbestos, lead-based paint, and other hazardous material removal and packaging

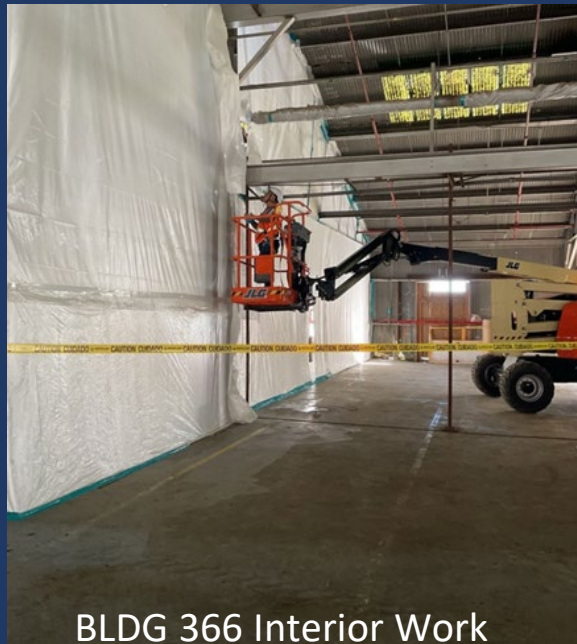

BLDG 366 Interior Work



BLDG 366 Lead abatement and covering

HPNS Parcel G
11 Mar 2026, 08:30:12

Parcel G Building Demolition Progress

Hazardous materials abatement has begun with Asbestos, lead-based paint, and other hazardous material removal and packaging



BLDG 366 Interior Work



BLDG 351A Crawl Space Abatement

Parcel G Building Demolition Progress

Shipment of waste out of state has begun

- All trucks are weighed and scanned for radiation prior to leaving HPNS



Truck Scale at Parcel G



Loading of asbestos pipe



Pre-staged sacks waiting to be loaded

NAVFAC Parcel G Contract Requirements for Local Hiring and Subcontracting



Contract Requirements *(Reference: Amendment 0010, RFO Part 1, Paragraph 3, Local Hiring Requirement, 10/03/24)*

- A minimum of 23% of all On-Site Work shall be subcontracted to local D-10 businesses
- A minimum of 23% of all On-Site Labor will be comprised of local-residents
- Eligible businesses must be located within ZIP Codes 94107, 94124, or 94134



Important

- The 23% requirement applies only to work physically performed at Parcel G (“On-Site Work”).



Compliance

- These requirements will be monitored throughout the project and are intended to be completely met at the end of the project

Parcel G Building Demolition Task Order Requirements

What is On-Site Work?

- Demolition of Buildings
- Abatement of Hazardous Materials
- Installation of BMPs and Inspections
- Backfill and Asphalt/Site Restoration
- Air Monitoring
- Industrial Hygiene
- Geotechnical Field Testing
- Civil Surveying
- Janitorial and Portable Facilities Servicing
- Site Security
- Site set up of trailers, fences, electrical hook up



Parcel G Building Demolition Task Order Requirements

What is Off-Site Work?

- Work Plan Development
- Reports
- Trucking all debris to Landfills and Recyclers
- Disposal of all debris/waste at the Landfills
- Analytical Lab Testing
 - Air Sampling
 - Geotech
- Office Support
- Project Management



Parcel G Building Demolition Task Order Requirements

| | |
|----------------------------------------|------------------------|
| ECC Initial Contract Award | \$28,416,507.11 |
| Modification 001 (Final Report) | \$43,841.00 |
| Modification 002 (Community Relations) | \$125,252.00 |
| Modification 003 (Rad Air Monitoring) | \$1,560,716.96 |
| Total Value = | \$30,146,317.07 |

Parcel G Building Demolition Task Order Requirements

How Is the On-Site Work Value Calculated?

| | Contract Value | Off-Site Value |
|-------------------|------------------------|------------------------|
| ECC Initial Award | \$28,416,507.11 | \$9,676,402.06 |
| Modification 001 | \$43,841.00 | \$43,841.00 |
| Modification 002 | \$125,252.00 | \$125,252.00 |
| Modification 003 | \$1,560,716.96 | \$839,202.91 |
| Totals | \$30,146,317.07 | \$10,684,697.97 |

12
34

Calculation Method

On-Site Work Value = Total Contract Value – Total Off-Site Work Value

On-Site Work Value = \$30,146,317.07 – \$10,684,497.97

On-Site Work Value = **\$19,461,619.00**

Parcel G Building Demolition Task Order Requirements

How much is the On-Site Work Worth?

On-Site Work Calculation:

Contract Award (minus) Off-Site Work Value = On-Site Work Value

| | |
|-----------------------------------|-------------------------|
| ECC Contract Award | \$30,146,317.07 |
| Total Off-Site Work | -\$10,684,697.97 |
| Total On-Site Work Value = | \$19,461,619.10 |

Parcel G Building Demo 23% Calculation

| | |
|---------------------------|------------------------|
| ECC Contract Award | \$30,146,317.07 |
| Total Off-Site Work | \$10,684,697.97* |
| Total On-Site Work | \$19,461,619.10 |

12 **34** Calculation Method

23% Contract Requirement = Total On-Site Work Value x 23%

23% Contract Requirement = \$19,461,619.10 x 0.23

23% Contract Requirement = **\$4,476,172.37**

*offsite work value projection

Local D-10 Current Subcontractor Awards

| D-10 Business | Zip Code | Scope of Work | Subcontract \$\$ Value |
|----------------------------|----------|--------------------------|---------------------------|
| Yerba Buena | 94124 | Site Restoration | \$4,701,782 |
| Aurora Environmental | 94134 | Industrial Hygiene | \$541,759 |
| Pacific Engineering | 94107 | SWPPP & Waste Management | \$486,000 |
| Armada Protective Services | 94107 | Security Services | \$344,717 |
| TBS Site Services | 94124 | Site Services | \$30,712 |
| Dyna Electric | 94134 | Electrical Services | \$9,974 |
| Total | | | <u>\$6,114,944</u> |

Calculation = (Total Subcontracted \$\$ Value ÷ Total On-Site Work Value)

$$(\underline{\$6,114,944} \div \underline{\$19,461,619.10}) = 0.314$$


$$0.314 \times 100 = \mathbf{31.4\%}$$

31.4% of the contract value has been awarded to D-10 Businesses

Local D-10

Current Subcontractor Dollars Spent

| D-10 Business | Subcontract \$\$ Value | Current \$\$ Spent Thru March 2026 | Remaining \$\$ on Contract |
|----------------------------|------------------------|------------------------------------|----------------------------|
| Yerba Buena | \$4,701,782 | \$0 | \$4,701,782 |
| Aurora Environmental | \$541,759 | \$41,848 | \$499,911 |
| Pacific Engineering | \$486,000 | \$38,800 | \$447,200 |
| Armada Protective Services | \$344,717 | \$35,366 | \$309,351 |
| TBS Site Services | \$30,712 | \$7,887 | \$22,824 |
| Dyna Electric | \$9,974 | \$12,942 | \$0 |
| Total | \$6,114,944 | \$136,843 | \$6,008,812 |

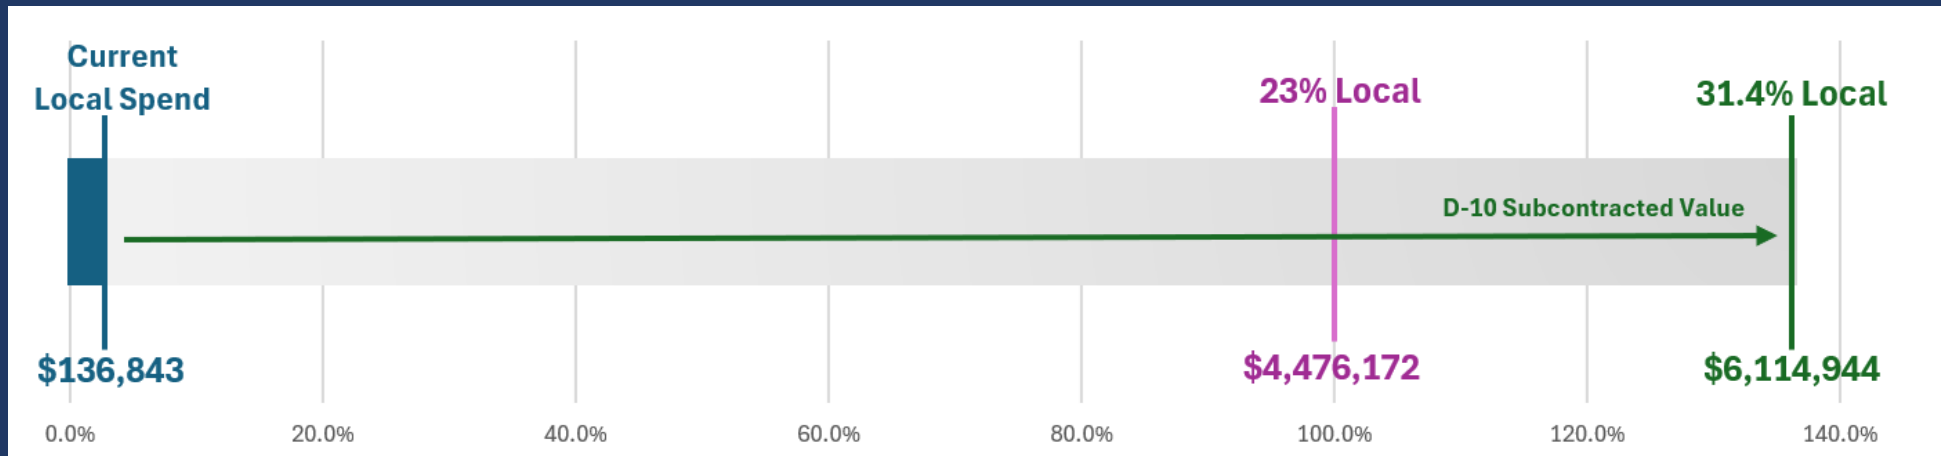

Local D-10 Procurement – Upcoming Opportunities

Still to be Awarded:

- Office Trailers Janitorial Services *(pending award)*
- Geotechnical Testing
- Civil Surveying



Local D-10 Current Procurement and Purchase Orders

ECC is committed to supporting the local community by prioritizing purchases from qualified D-10 businesses and local stores for the Parcel G Building Demolition Project.

| D-10 Business | Zip Code | Purchase Order \$\$ Value | Current \$\$ Spent |
|----------------------------------|----------|------------------------------|-----------------------|
| JRM Equipment Rental | 94124 | \$235,950.00 | \$33,675.44 |
| Center Hardware & Supply Company | 94107 | \$10,000.00 | \$3,777.18 |
| Level Construction Supply | 94124 | \$10,000.00 | \$5,785.81 |
| Total | | \$255,950.00 | \$43,238.43 |

This commitment will continue throughout the duration of the Parcel G project


Meeting the 23% Local Workforce Requirement

Employment Opportunities by Firm /Trade through March 2026

| Firm | Trade-Employment Category | # of Workers on Site | # Local Employees | Local % |
|----------------------------|---------------------------------------|----------------------|-------------------|---------|
| Pacific Engineering | SWPPP Inspectors & Waste Coordinators | 2 | 2 | 100% |
| Bayview | Craft Union Abatement Workers | 29 | 11 | 37.9% |
| Aurora Environmental | Environmental Technicians and CAC | 3 | 1 | 33.3% |
| Armada Protective Services | Security Guards | 5 | 4 | 80.0% |
| Dyna Electric | Electrical Services | 1 | 1 | 100.0% |
| TBS Services | Portable Facilities Servicing | 4 | 3 | 75.0% |
| | Totals: | 44 | 22 | 50% |

Calculation = (total local workers/total workers) x 100 = 50%

Meeting the 23% Local Workforce Requirement

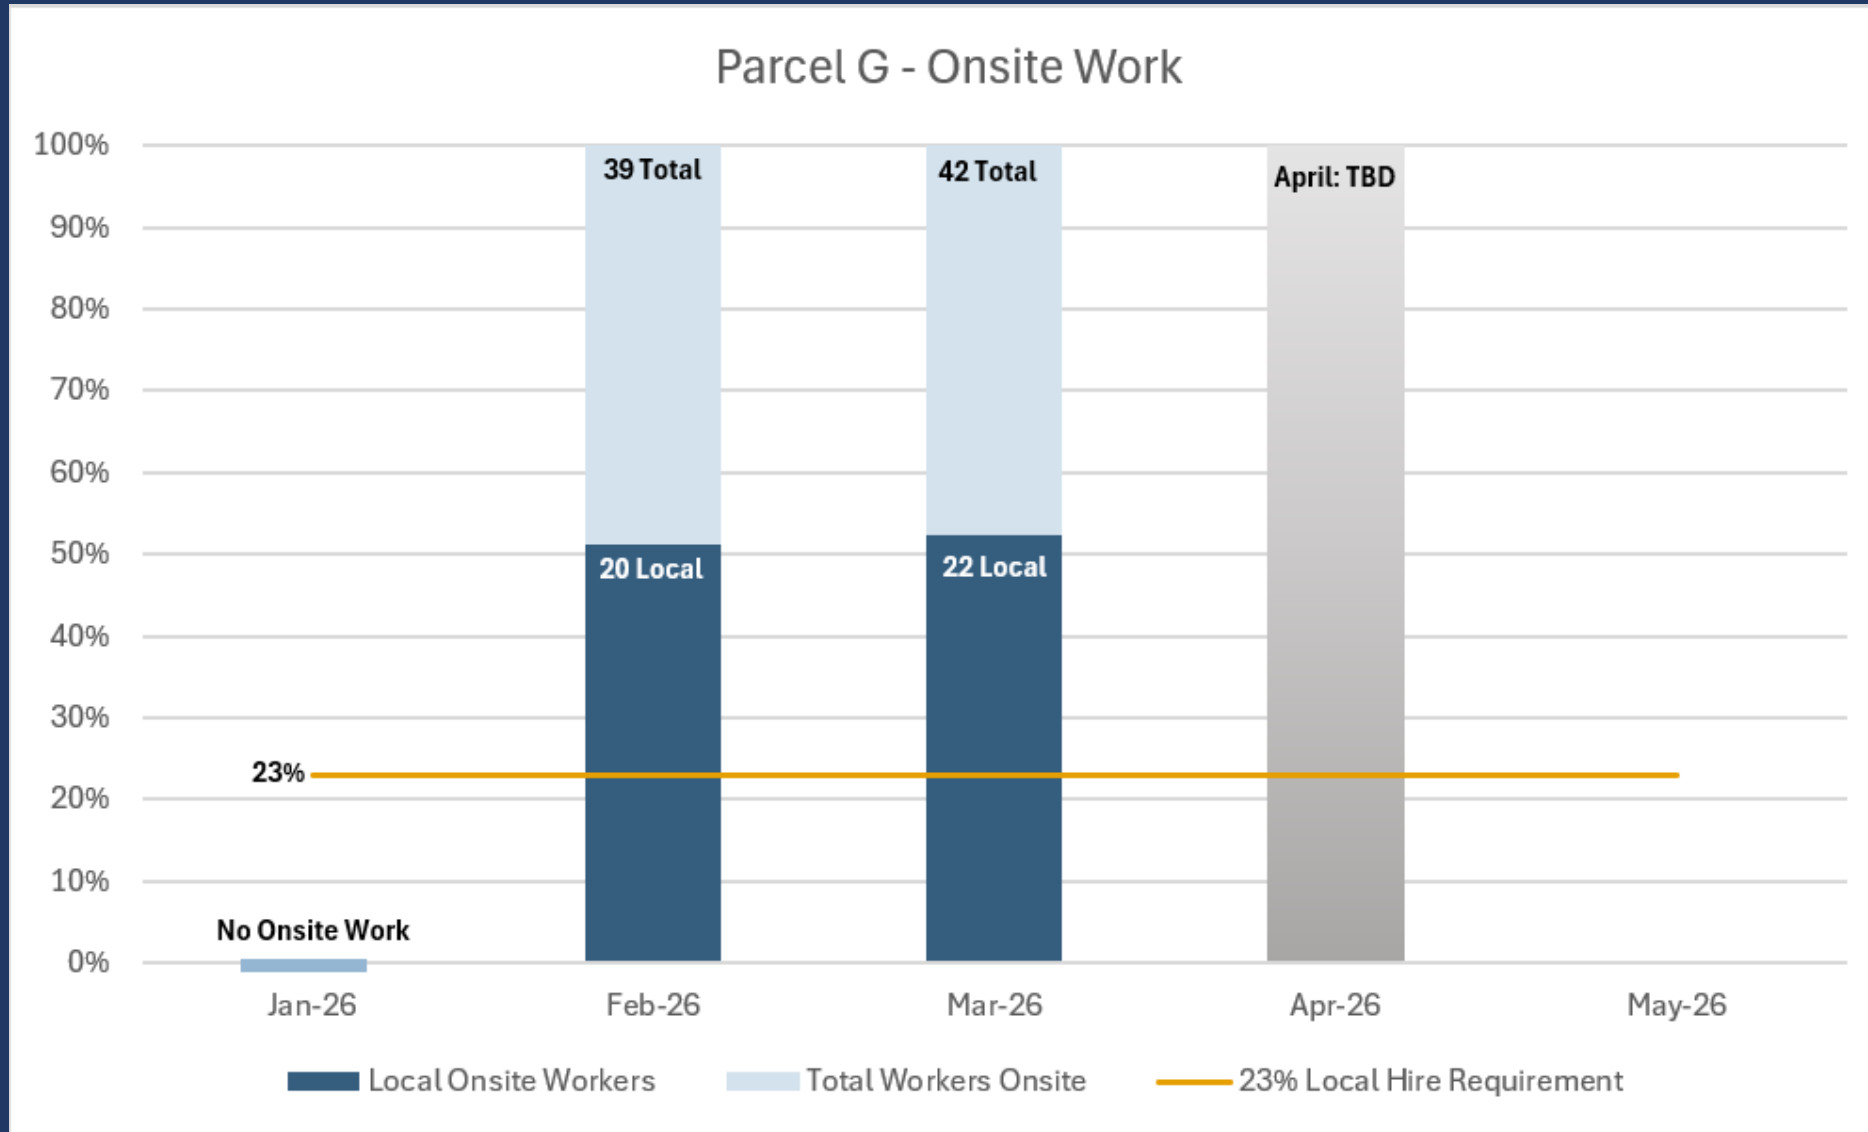

Parcel G TO: Internship Program Update

Two local interns have been hired. Both were referral from the CAC Committee and local Community Groups.

- #1: Started on March 31, 2026
- #2: Summer Position



There are still opportunities for Fall and 2027

Parcel G TO: Internship Program

- ECC has a successful college paid internship program executed throughout the nation
- For HPNS Parcel G task order, ECC will seek to add one or two college internships in early 2026 to continue throughout the calendar year
- Seeking eligible Construction Management or Engineering candidates
 - Junior or Senior year candidates are eligible
 - A minimum 3.0 GPA
- This is a rolling position, and this opportunity will be available through out 2026 - 2027



Scan this code to apply!

CAC B&E Meeting Schedule

ECC is contracted to attend three (3) CAC B&E Meetings Annually

January, April, and September 2026

September 2026

- Project Schedule Update
- 23% Requirement Progress
- Update on Subcontracting Opportunities
- Internship Update

Future Work with ECC

There is more future work beyond Parcel G!

ECC has four other contracts with the NAVFAC Southwest.

As task orders are released, companies that are registered with us will be contacted and given the opportunity to bid for work at HPNS and other Navy facilities in the Bay Area.



Parcel G TO: *Follow Us for Updates!*




@ECCCorp



@ECC_Corp



@ECC.HQ



Parcel G Contacts

ECC Infrastructure LLC



Project Manager – Kaiulani Watson, PG
Contracts Manager – Elizabeth Webb

700 Airport Blvd, Suite 250
Burlingame, CA 94010



HPNSContracts@ecc.net



(415) 769-0122



Parcel G Building Demolition – Contracting Compliance Monitoring Navy - ROICC

Compliance Monitoring - 23% Labor Requirement

- **Certified Payrolls**

- **The Davis-Bacon Act (DBA) requires federally-funded construction projects in excess of \$2,000 to abide by the locally prevailing wage rates as determined by the Department of Labor.**
- **In general, the DBA applies to manual laborers rather than professional services (e.g. blue collar vs white collar), and are determined based on the following factors:**
 - Geographic Area
 - Construction Type
 - Labor Classification
- **DBA is intended to make sure that laborers categorized under the DBA are not underpaid.**
- **Certified payrolls are submitted to demonstrate compliance with DBA.**
 - Specifically Davis-Bacon Act Wage Determination #CA20250018, available on SAM.gov


Compliance Monitoring - 23% Labor Requirement

- **Non-DBA Certification**

- **Subcontractors providing employees that do not fall under a DBA labor classification send a letter of certification with employee names and their home ZIP codes.**
- **Unlike the certified payrolls, these letters of certification do not include the number of hours worked during the invoice period, the type of work performed by the employee, or their labor rate.**
- **Currently in the process of receiving non-DBA payrolls from the contractor.**

Compliance Monitoring - 23% Labor Requirement

• Certification Letter Example



March 31, 2026

Ms. Gina Hossman, Contracting Officer
 Travis ROICC, Code: ROPWT
 Travis Air Force Base
 191 W. St.
 Travis AFB, CA 94535-0597



Subject: On-Site Local Labor Requirement


Contract No: N62473-21-D-1205, Task Order N62473-25-F-4397
 Parcel G Building Demolition at BRAC Former Hunters Point Naval Shipyard,
 San Francisco, California

Dear Ms. Hossman:
TBS Site Services is a subcontractor that is providing on-site labor to ECC Infrastructure LLC (ECC) on the above-reference contract for Parcel G Building Demolition. We are certifying that the employees listed below are not covered under Wage Determination #: General Decision Number CA20250018 Modification No. 6 dated 03/21/2025, therefore no certified payrolls are generated. We have verified their zip code of residence as part of the 23% local hiring requirement.

| Employee Name | Employee's Home Zip Code |
|---------------|--------------------------|
| [REDACTED] | 94124 |
| [REDACTED] | 94124 |
| [REDACTED] | 94112 |
| [REDACTED] | 94124 |

Sincerely,
Anita J Butler
 Anita Butler
 CEO
 TBS Site Services
Portable Restroom Services
 Our Service. Your Success

For further information, please contact us:
 1275 Fair Avenue Suite 202 San Francisco 94124
 415-724-1802 (c) 1-833-482-7178 (o)



701 Pennsylvania Avenue
 San Francisco, California 94107
 www.armadasecurity.com

Main 415.647.8500
 Fax 415.643.0991

March 30, 2026


Ms. Gina Hossman, Contracting Officer
 Travis ROICC, Code: ROPWT
 Travis Air Force Base
 191 W. St.
 Travis AFB, CA 94535-0597

Subject: On-Site Local Labor Requirement

Contract No: N62473-21-D-1205, Task Order N62473-25-F-4397
 Parcel G Building Demolition at BRAC Former Hunters Point Naval Shipyard,
 San Francisco, California

Dear Ms. Hossman:
Armada Protective Services Inc is a subcontractor that is providing on-site labor to ECC Infrastructure LLC (ECC) on the above-reference contract for Parcel G Building Demolition. We are certifying that the employees listed below are not covered under Wage Determination #: General Decision Number CA20250018 Modification No. 6 dated 03/21/2025, therefore no certified payrolls are generated. We have verified their zip code of residence as part of the 23% local hiring requirement.

| Employee name | Employee Home Zip Code |
|---------------|------------------------|
| [REDACTED] | 94107 |
| [REDACTED] | 94107 |
| [REDACTED] | 94109 |
| [REDACTED] | 94124 |
| [REDACTED] | 94134 |

Sincerely,

 Mikhail Butenko
 Manager
 Armada Protective Services Inc

PACIFIC ENGINEERING & CONSTRUCTION, INC.
Consulting Engineers & Contractors
 470 3rd Street, Suite 105 San Francisco, CA 94107
 Phone/fax (415) 974-1853
 Cell (415) 516-8545
 California Professional Engineering License # 38905
 California Contractor State License Board # 858547 (A, B, Haz)
 Nevada Professional Engineering License # 17624
 Nevada Certified Environmental Manager #1870

March 28, 2026

Ms. Gina Hossman, Contracting Officer
 Travis ROICC, Code: ROPWT
 Travis Air Force Base
 191 W. St.
 Travis AFB, CA 94535-0597

Subject: On-Site Local Labor Requirement

Contract No: N62473-21-D-1205, Task Order N62473-25-F-4397
 Parcel G Building Demolition at BRAC Former Hunters Point Naval Shipyard,
 San Francisco, California

Dear Ms. Hossman:
 Pacific Engineering & Construction, Inc. is a subcontractor that is providing on-site labor to ECC Infrastructure LLC (ECC) on the above-reference contract for Parcel G Building Demolition. We are certifying that the employees listed below are not covered under Wage Determination #: General Decision Number CA20250018 Modification No. 6 dated 03/21/2025, therefore no certified payrolls are generated. We have verified their zip code of residence as part of the 23% local hiring requirement.

| Employee Name | Employee's Home Zip Code |
|---------------|--------------------------|
| [REDACTED] | 94124 |
| [REDACTED] | 94124 |
| [REDACTED] | |
| [REDACTED] | |

Sincerely,
A. Mark Waldman
 A. Mark Waldman
 President
 Pacific Engineering & Construction, Inc.

Compliance Monitoring - 23% Labor Requirement

- **Labor Interviews**
 - **The ROICC conducts labor standards interviews randomly for workers on site. These interviews ensure that the Government and workers can have a truthful discussion on the workers' labor standards without influence from the contractor.**
 - **Labor interviews are conducted utilizing the Standard Form 1445.**

Compliance Monitoring - 23% Labor Requirement

- Standard Form 1445

| LABOR STANDARDS INTERVIEW | | | | | | |
|-------------------------------------------------------------------------------------------------------------|------------|---------------------------------------------------------|---------------------|--------------------------|--------------------------|--------------------------|
| CONTRACT NUMBER | | EMPLOYEE INFORMATION | | | | |
| NAME OF PRIME CONTRACTOR | | LAST NAME | FIRST NAME | MI | | |
| NAME OF EMPLOYER | | STREET ADDRESS | | | | |
| SUPERVISOR'S NAME | | CITY | STATE | ZIP CODE | | |
| LAST NAME | FIRST NAME | MI | WORK CLASSIFICATION | WAGE RATE | | |
| ACTION | | | | | CHECK BELOW | |
| | | | | | YES | NO |
| Do you work over 8 hours per day? | | | | | <input type="checkbox"/> | <input type="checkbox"/> |
| Do you work over 40 hours per week? | | | | | <input type="checkbox"/> | <input type="checkbox"/> |
| Are you paid at least time and a half for overtime hours? | | | | | <input type="checkbox"/> | <input type="checkbox"/> |
| Are you receiving any cash payments for fringe benefits required by the posted wage determination decision? | | | | | <input type="checkbox"/> | <input type="checkbox"/> |
| WHAT DEDUCTIONS OTHER THAN TAXES AND SOCIAL SECURITY ARE MADE FROM YOUR PAY? | | | | | | |
| HOW MANY HOURS DID YOU WORK ON YOUR LAST WORK DAY BEFORE THIS INTERVIEW? | | | TOOLS YOU USE | | | |
| DATE OF LAST WORK DAY BEFORE INTERVIEW (YYMMDD) | | | | | | |
| DATE YOU BEGAN WORK ON THIS PROJECT (YYMMDD) | | | | | | |
| THE ABOVE IS CORRECT TO THE BEST OF MY KNOWLEDGE | | | | | | |
| EMPLOYEE'S SIGNATURE | | | | | DATE (YYMMDD) | |
| INTERVIEWER | SIGNATURE | TYPED OR PRINTED NAME | | DATE (YYMMDD) | | |
| INTERVIEWER'S COMMENTS | | | | | | |
| WORK EMPLOYEE WAS DOING WHEN INTERVIEWED | | ACTION (if explanation is needed, use comments section) | | YES | NO | |
| | | IS EMPLOYEE PROPERLY CLASSIFIED AND PAID? | | <input type="checkbox"/> | <input type="checkbox"/> | |
| | | ARE WAGE RATES AND POSTERS DISPLAYED? | | <input type="checkbox"/> | <input type="checkbox"/> | |
| FOR USE BY PAYROLL CHECKER | | | | | | |
| IS ABOVE INFORMATION IN AGREEMENT WITH PAYROLL DATA? | | | | | | |
| <input type="checkbox"/> YES <input type="checkbox"/> NO | | | | | | |
| COMMENTS | | | | | | |
| | | | | | | |
| CHECKER | | | | | | |
| LAST NAME | FIRST NAME | MI | JOB TITLE | | | |
| SIGNATURE | | | | | DATE (YYMMDD) | |
| AUTHORIZED FOR LOCAL REPRODUCTION | | | | | | |
| STANDARD FORM 1445 (REV. 12-66) | | | | | | |
| Previous edition not usable Prescribed by GSA - FAR (48 CFR) 53.222(g) | | | | | | |

Compliance Monitoring - 23% Subcontracting Requirement

- **Local Business**

- **The contractor's local business completed work values shown earlier are compared to the following:**

- The contractor's invoice request
- The contractor's daily production reports
- The contractor's quality control reports
- The ROICC's daily site visits

- **This ensures alignment between the work completed on site, the work being charged for invoicing, and the proper assignment of work to the appropriate subcontractor.**

Compliance Monitoring - 23% Local Requirements

- **Consequences**

- **If supporting documentation and labor interviews do not comply with contract requirements, payment to the contractor will either be reduced or withheld completely until the deficiency is corrected.**



Hunters Point New Building Demolition MACC Navy - BRAC

Hunters Point Naval Shipyard (HPNS)
Navy Base Realignment and Closure (BRAC)



New HPNS Building Demolition MACC

- Multiple award construction contract (MACC) awarded February 5, 2026
- Task orders for future building demolition projects will be awarded against this basic contract
- Contract has five awardees
 - RSI Amentum Environmental Solutions, LLC (San Francisco, CA)
 - Aptim Radiological Services LLC (San Diego, CA)
 - ECC Expeditionary Constructors LLC (Burlingame, CA)
 - Ferma Corporation (Newark, CA)
 - Integrated Demolition and Remediation Inc. (Anaheim, CA)
- Some awardees have started company specific outreach to the local community for hiring and subcontracting opportunities.

Next HPNS Building Demolition Task Order

- Planned for Parcel B – 5 buildings, Parcel C – 1 building
- Awarding task order for developing the scope of work language for the Request for Offers (RFO), this effort includes a hazardous materials assessment of each building
- RFO development anticipated to require 6-9 months
- Planning to have an industry day similar to the one held for Parcel G
- Building Demolition Information Hub maintained on the HPNS website, sign up for email notifications for when new information is posted

Resources for More Information

HPNS Program Management



Michael Pound
michael.j.pound.civ@us.navy.mil

Navy BRAC PMO West
33000 Nixie Way, Bldg 50, Suite 207
San Diego, CA 92147
www.bracpmo.navy.mil/hpns

Regulatory Agencies

US Environmental Protection Agency

Mike Collins: collins.mike@epa.gov
Nadia Burke: burke.nadiahollan@epa.gov

CA Dept. of Toxic Substances Control

Michael Howley: michael.howley@dtsc.ca.gov

San Francisco Bay Regional Water Quality Control Board

Mary Snow: mary.snow@waterboards.ca.gov

Other Resources



Community Technical Advisor
Dr. Kathryn Higley
(541) 737-0675

kathryn.higley@oregonstate.edu
www.ne.oregonstate.edu

HPNS Online Information Repository



- <https://www.bracpmo.navy.mil/hpns>
- <https://administrative-records.navfac.navy.mil/?PN24V63WGTUM4VG4WO>

HPNS Community Outreach

Send an email or leave a message

- For program information
- To join the HPNS Mailing List
- To request language assistance



info@sfhpns.com



(415) 295-4742
